


Farrington Highway Stations Group 85% Complete

Contract Completion: July '18
Hō'ae'ae (West Loch) Station – 89% Complete

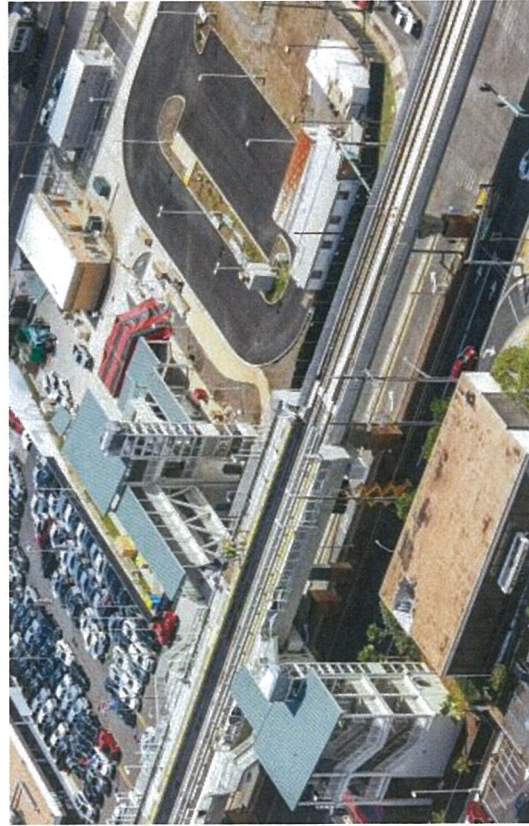

Major Work Remaining

- Platform topping slab
- Entrance tile
- Canopies
- Platform CSC cabinets

Energyization Status

- Station and TPSS - Complete

Core Systems Interface

- BoS Date – March 19, 2019
- TCCR access has been provided.

Platform Partial Access - March 17, 2019


Canopy installation - August 2019

Farrington Highway Stations Group

85% Complete

Contract Completion: July '18

Pouhala (Waipahu Transit Center) Station – 83% Complete

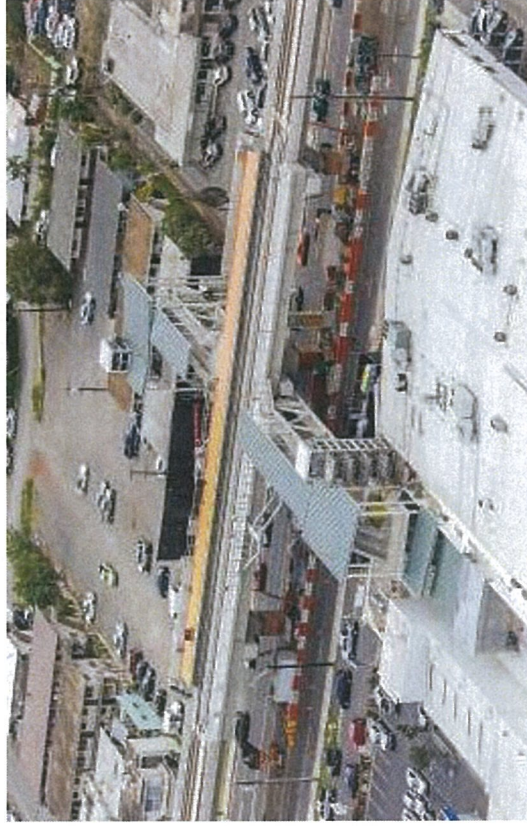

Major Work Remaining

- Platform topping slab pour
- Moloalo Street entrance
- Makai ground floor slabs
- Makai electrical chase
- Platform CSC cabinets
- Canopies

Energization Status

- Station and TPSS - Complete

Core Systems Interface

- BoS Date - April 19, 2019
- TCCR access provided.

Platform Partial Access - March 2019


Canopy Installation - June 2019



Farrington Highway Stations Group

85% Complete

Contract Completion: July '18
 Hālaulani (Leeward Community College) Station – 82% Complete

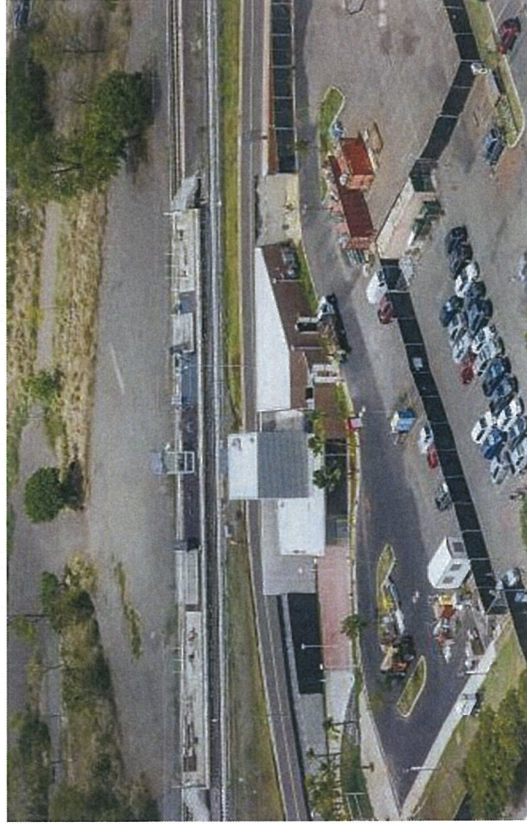

Core Systems Interface

- AHJV is currently working in the UPS room
- BoS Date - May 2019
- TCCR access provided.

Major Work Remaining

- Platform topping slab
- Parking lot repairs
- Platform CSC Cabinets
- Canopies

Energization Status

- Station and TPSS – infrastructure and easement



University of Hawaii Park and Ride - Road "B"


56.8% Complete

Contract Completion: July '19



WOSG Group interface

- Main power connection & tie into the UHWO Station
- Traffic signals

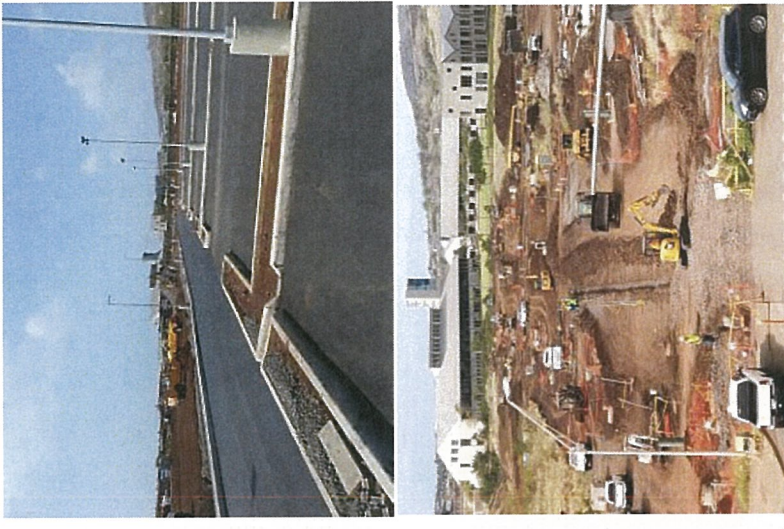

Major Work Remaining

- Base Course Installation for Road B
- Paving of Road "B" and Park & Ride
- Traffic signals For Road B
- PCCP paving for TP&R
- Bus Shelter installation TP&R
- Final Lift of AC paving for the parking lot TP&R



Core Systems 62% Complete

Projected Completion
October 2025



Testing

- Integration testing of the interfaces between the vehicle & wayside Comms and control equipment is expected to begin in 2nd Q 2019.

Testing in Progress

- Wayside ATC testing in West Loch is ongoing.
- The PV Fire re-test of the floor and roof is scheduled for April 2019.

MSF Yard

- AHJV communication team restructure plans in progress.

Platform Screen Gates

- East Kapolei PSGS tower installation completed.



Manufacturing

- All Signal, TES, and SCADA systems are onsite or ready for delivery for Segment 1.
- Pearlridge and Aloha Stadium TPSS onsite delivery schedule in progress.
- Train #6 delivered to MSF on March 3, 2019.

Airport Guideway and Stations

41.5% Complete



Contract Completion: May 2021

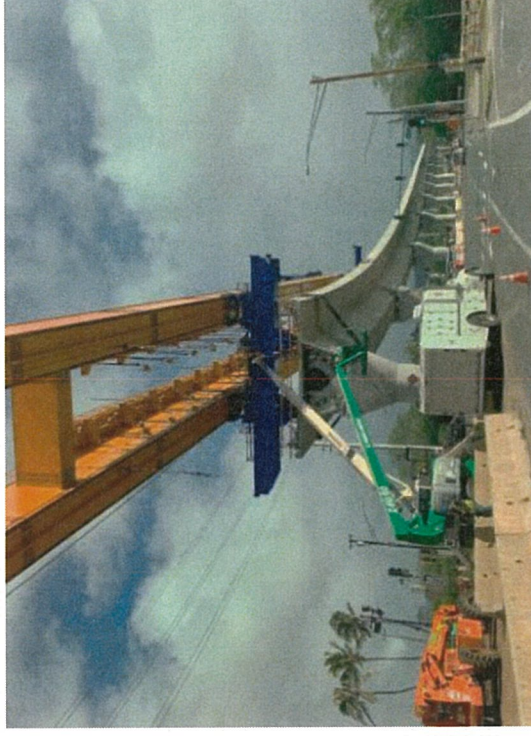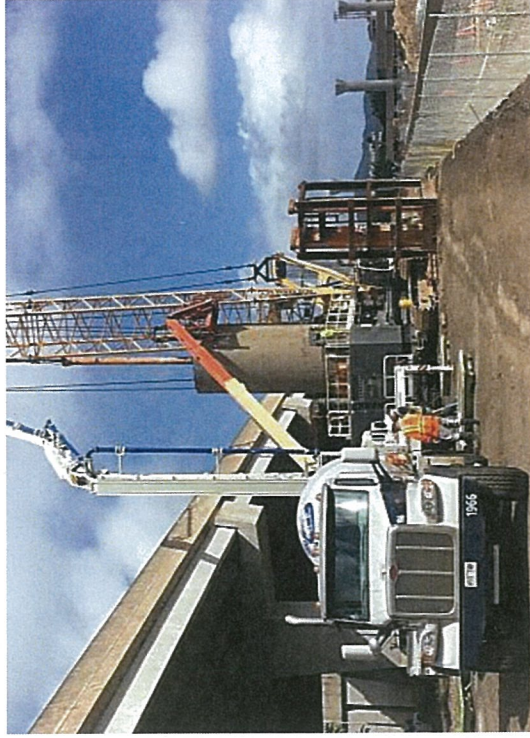

- **Completed To Date:** Design progression at 99%. 134 drilled shaft foundations Completed, 99 columns installed, and 13 spans have been erected. 1,294 pre-cast segments have been cast. Electrical infrastructure and cabling work was completed in HECO Zone 5 (Nimitz Highway and Aolele Street.)
- **Ongoing Construction:** Rebar erection/formwork and anti-graffiti coating application for Reach A, B, and C Columns, drilling for deep foundation shafts in Reach E. Gantry operations for span erection to continue in Reach A and the erection of the second gantry for Reach C at the airport has been initiated.

City Center Utilities Relocation

Status as of February 20, 2019

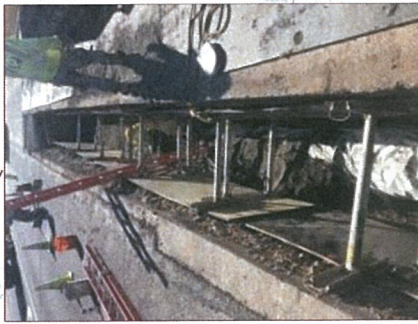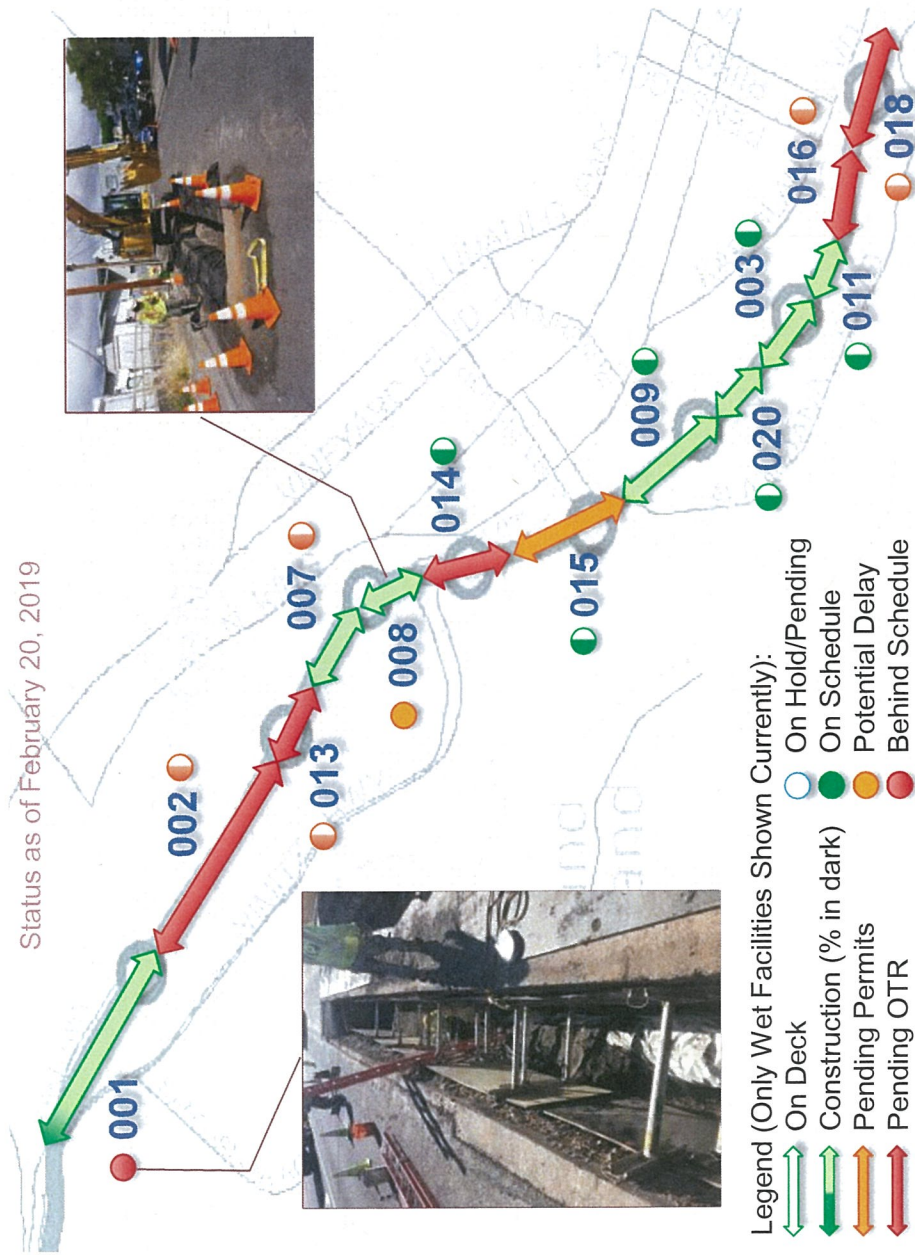

- Installed Work Progress (Estimate): **1.0%** vs 0.8% last update
- Estimated Completion: February 2022
- Highlights on Active Task Orders:
 - **001** – Relocating 24” water facility, over 200’ installed
 - **008** – Excavating for Water/Sewer/Drainage facilities
 - **011** – Relocating drainage facility
 - **014/015** – Awaiting DPP OTR and/or HDOT Permits
 - **016/018** – Probing for dry and wet facilities; Awaiting DPP OTR
- Highlights on Design Finalization Issues:
 - **Dillingham Dry** – design being Completed; working on spacing and combining comms line; alternatives are being vetted that may reduce the overall scope.
 - **Halekauwila Wet/Dry** – Impacts being assessed for keeping 46kV on Halekauwila and integrating straddles between Cook and Ward.
 - **Roadway Design** – Awaiting OTR.

Stay Connected

- Weekly Traffic Advisories
- Weekly e-Blast
- Website and Social Media



HART
HONOLULU AUTHORITY INC. RAPID TRANSPORTATION

HART WEEKLY eNEWS
March 2, 2018

HART & ANSALDO HONOLULU JV REACH MAJOR MILESTONE IN RAIL PROJECT

HART & Ansaldo Honolulu Joint Venture reached a critical milestone this week in the completion of the Honolulu Rail Transit Project and the start-up of operations



HART Rapid Response:

- 24-Hour Project Hotline number 808-566-2299
- Email Inquiries: info@HonoluluTransit.org
- Social Media Inquiries

Mahalo!

Ho, Diana C

From: Kraintz, Franz <fkraintz@honolulu.gov>
Sent: Friday, March 22, 2019 2:29 PM
To: Ho, Diana C
Cc: Fink, John
Subject: Monthly report

Nothing new to report on the Halawa Area TOD Plan. The state infrastructure study is making progress. They have developed some scenarios and are analyzing them to come up with a preferred scenario in the coming months. That meeting was in mid-February and Charlie V. may have mentioned it in his report last meeting.

I will try to make it next week. Have a great weekend.

Franz Kraintz, AICP
Planner, Community Planning Branch
Dept of Planning and Permitting
City & County of Honolulu
650 S. King Street
Honolulu, Hawaii 96813
Ph. 808 768 8046 (O)
fkraintz@honolulu.gov

HIC-TOD Report
For
Stadium Authority Board Meeting
28 Mar 2019

1. HIC-TOD Meeting 12 Mar 2019
 - a. Review and update of 2019 TOD Legislation presented
 - b. Infrastructure Update for 3 top priority areas: East Kapolei, Halawa-Stadium, Iwilei-Kapalama
 - c. Submittal of Permitted Interagency Group (PIG) reports for above mentioned areas for acceptance by Council
 - d. Neighborhood Islands PIG reformed for 2019

2. Next meeting: 9 April 2019
 - a. Oahu Permitted Interaction Group to be reformed
 - b. Review and update of 2019 TOD Legislation to be presented

Stadium Authority Board Bill Tracking as of 03/22/19

Measure Number	Status	Stadium Authority Position	Comments
SB 997, SD2, HD1	03/15/19 – Passed 2 nd reading w/ amendments. (LAB, WLH, JUD, FIN)	Support	Expands the powers and duties of the stadium authority to develop the stadium property and establish a stadium complex area development plan. (\$50M/\$150M/\$150M)
SB 1530, SD3, HD1	02/26 – Passed 2 nd read as amended in HD1 (LAB, WLH, JUD, FIN)	Support	Establishes the stadium development district, which includes all state property under the jurisdiction of the stadium authority, and places that property under the jurisdiction of the Hawaii community development authority for development purposes.
HB 1497, HD3, SD1	03/22 – EET rec pass 2 nd read, as amended, referred to WAM. (EET, WAM).	Support	Authorizes the issuance of revenue bonds and special facility revenue bonds and appropriates funds. Exempts the stadium development district from section 206E-5, HRS. Authorizes the department of land and natural resources to give written concurrence on any project in the stadium development district based on a phased review. (SD1) (\$50M/\$150M/\$150M)
HB 1259, SD1 (H&S CIP)	03/19 – (S) WAM recv'd notice of disagree (WAM)	Monitoring to address \$20M-C/\$10M-C	Appropriates capital improvement projects for fiscal biennium 2019–2021. Funding @ Health & Safety (\$10k C/\$10k C).

SB 859, SD1 (H&S CIP)	03/19 – Referred to FIN, (FIN)	Monitoring	Authorizes funds for capital improvement projects for the fiscal biennium 2019-2021 Health & Safety (\$10k C//\$10k C)
HB 2, HD1, SD1 (Operating Budget)	03/22 – Reconvene conference-comm. (Conf)	Support	RELATING TO THE STATE BUDGET. Appropriates funds for the operating budget of the Executive Branch for fiscal years 2019-2020 and 2020-2021.
SB 126, SD1 (Operating & CIP Budget) (now shell for misc. GM, etc.)	03/21 – (H) EEP deferred (EEP, FIN)	Support	Appropriates funds for the operating and capital improvement budget of the Executive Branch for fiscal years 2019-2020 and 2020-2021.
HB 964 (Budget)	04/28 – Referred to FIN – dead.		
HB 116, SD1 (Operating Budget – other)	03/20 – Conference comm (Conf)	Monitoring	Relating to the State Budget (excludes Stadium Operating)
SB 1110, SD1 (Budget)	02/13 – Referred to WAM (Did not cross – dead)	Support	Appropriates funds for various capital improvement projects to be expended by the department of accounting and general services. (SD1)
SB 290 (Budget)	02/28 – WAM deferred – dead (WAM)	Support	Appropriates funds for the operating budget of the Executive Branch for fiscal years 2019-2020 and 2020-2021.

<p>HB 1432, HD1 (Operating Budget)</p>	<p>03/08 – Re-referred. (GVO/TEC, WAM)</p>	<p>Monitor - DAGS operating (excludes Stad op.)</p>	<p>Appropriates funds for the fiscal biennium 2019-2021 operating budget of certain programs of the Department of Accounting and General Services programs under the purview of the House of Representatives Standing Committee on Legislative Management. (HB1432 HD1)</p>
<p>HB 1426, HD1 (Operating Budget)</p>	<p>03/19 – GVO/TEC deferred. (GVO/TEC, WAM)</p>	<p>Monitoring DAGS Budget (Removed/Excludes AGS-889 CIP in HD1)</p>	<p>RELATING TO THE DEPARTMENT OF ACCOUNTING AND GENERAL SERVICES. Provides funding for the operations of the Department of Accounting and General Services for Fiscal Biennium 2019-2021. (HB1426 HD1)</p>
<p>HB 889, HD1, SD1 (P3)</p>	<p>03/22 – GVO rec pass as amended in SD2. Referred to WAM (GVO, WAM)</p>	<p>No position taken Monitoring</p>	<p>Establishes the Office of Public-Private Partnership and the position of Public-Private Partnership Coordinator. Adds public-private partnership project delivery methods and related conditions and requirements to the Hawaii Public Procurement Code. Requires an annual report. Appropriates funds. (HB889 HD1)</p>
<p>SB 653, SD1, HD1 (EV)</p>	<p>03/21 – Passed 2nd read as amended in HD1. (EEP/TRN, FIN)</p>	<p>Monitoring</p>	<p>Requires certain new state building construction and county building construction projects to dedicate at least twenty per cent of its total projected amount of parking stalls to be electric vehicle charger ready and requires that all new state</p>

			<p>building construction and county building construction have at least two electric vehicle charger ready parking stalls. (SD1)</p>
<p>SB 1389, SD1 (TOD infrastructure)</p>	<p>02/20 – WAM – Passed with amendments.</p>	<p>No position Monitoring measure</p>	<p>Authorizes the Hawaii Housing Finance and Development Corporation (HHFDC), at the request of the Hawaii Community Development Authority (HCDA), to establish and operate transit-oriented development infrastructure improvement zone subaccounts within the dwelling unit revolving fund for the benefit of infrastructure improvement projects within a transit-oriented development infrastructure improvement zone. Requires HCDA to develop a transit-oriented development infrastructure improvement zone program to foster infrastructure development by strategically investing in public facilities. Appropriates funds to HCDA for staff necessary to develop and manage the transit-oriented development infrastructure improvement zone program. Effective 7/1/2050. (SD1)</p>
<p>HB 695</p>	<p>02/12 – Measure deferred – Dead</p>	<p>No position taken</p>	<p>Authorizes the issuance of general obligation bonds for the design and construction of a new stadium. Requires a one-third private sector funding match. Appropriates funds.</p>
