

**Monthly Summary of Events Report
Events Branch
10-18-19 to 11-8-19**

DATE	EVENT	LOCATION	ATTENDANCE	# OF USHERS	VEHICLES PARKED	# OF PARKING ATTENDANTS	OTHER EVENT(S) HELD ON SAME DATE/TIME	COMMENTS
10/19/19	UH vs Air Force	Stadium	20,217	149	5,797	94		UH - 26 vs Air Force - 56
10/25/19	ILH Football	Stadium	4,363	16	1,443	38		Punahou - 47 vs KS-Kapalama - 20 Iolani - 21 vs Damien - 14
10/26/19	OIA Football	Stadium	5,968	41	1218	35	Swap Meet	Roosevelt - 24 vs Kaimuki - 27 Moanalua - 21 vs Leilehua - 20 Miiilani - 3 vs Kahuku - 7
10/27/19	SCCA	Lower Halawa Parking Lot					Swap Meet	Defensive driver training.
10/28/19	Hawaii Jr. Prep Football	Stadium	1,569	7	521	4		Youth tackle football games.
10/30/19	Hawaii Jr. Prep Football	Stadium	920	7	346	5		Youth Tackle football games.
11/1/19	ILH Football	Stadium	4,257	19	1,525	38		St. Louis - 21 vs Punahou - 14
11/2/19	UH vs Fresno State	Stadium	18,293	145	5,072	100		UH - 38 vs Fresno State - 41
11/3/19	Oahu Pop Warner Football	Stadium	1,459	14	130	3	Swap Meet	Youth tackle football games.
11/4/19	Oahu Marching Band Festival	Stadium	2,423	23	720	24		High school marching band festival.

November 2019

December 2019

November 2019

Su	1	2	3	4	5	6	7
Mo	8	9	10	11	12	13	14
Tu	15	16	17	18	19	20	21
We	22	23	24	25	26	27	28
Th	29	30	31				

Su	3	4	5	6	7	8	9
Mo	10	11	12	13	14	15	16
Tu	17	18	19	20	21	22	23
We	24	25	26	27	28	29	30
Th							
Fr							
Sa							

SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
Oct 27	28	29	30	31	Nov 1	2
6:30am Swap Meet (Circle Lot) 7:30am Pop Warner (Stadium)	5:30pm Pearl City H.S. Music Learning Center (Stadium) 6:30pm OFOA (HR)	8:00am Pay 6:00pm HSBOA (HR)	8:00am Swap Meet (Circle Lot)		6:00pm ILH Playoff: St. Louis vs Punahou (Stadium)	8:00am Swap Meet (Circle Lot) 6:00pm UH vs Fresno State (Stadium)
3	4	5	6	7	8	9
6:30am Swap Meet (Circle Lot) 7:30am Pop Warner (Stadium) 4:00pm Carreira-Manin	HOLIDAY - Veterans' Day 4:30pm 40th Annual Marching Band Festival (Stadium)	12:00pm OJA Athletic Health Care Trainers	8:00am Swap Meet (Circle Lot)	3:00pm Video Shoot (Jordan Salud, Kyle Blas) (Stadium)	8:00am Swap Meet (Circle Lot) 6:00pm UH vs San Jose State (Stadium)	8:00am Swap Meet (Circle Lot) 6:00pm UH vs San Jose State (Stadium)
10	11	12	13	14	15	16
6:30am Swap Meet (Circle Lot) 7:30am Pop Warner (Stadium) 4:00pm Carreira-Manin	HOLIDAY - Veterans' Day 4:30pm 40th Annual Marching Band Festival (Stadium)	12:00pm OJA Athletic Health Care Trainers	8:00am Swap Meet (Circle Lot)	3:00pm Video Shoot (Jordan Salud, Kyle Blas) (Stadium)	7:30am DOE: Driver & Traffic Safety Education (LHPL) 8:00am Swap Meet (Circle Lot)	7:30am DOE: Driver & Traffic Safety Education (LHPL) 8:00am Swap Meet (Circle Lot)
17	18	19	20	21	22	23
6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot)	8:00am HFD (Stadium) 12:30pm HGFEA	7:00am DOH: Dignity of Risk Training (HR) 8:00am HFD (Stadium)	8:00am Pay 8:00am Swap Meet (Circle Lot) 12:00pm SoFi HI Bowl Executive Committee	9:00am DHS: Med-QUEST (HR)	4:00pm HHSAA Open Division Semi Finals: Kahuku vs Campbell 7:00pm HHSAA Open Division Semi Finals:	8:00am Swap Meet (Circle Lot) 6:00pm UH vs San Diego State (Stadium)
24	25	26	27	28	29	30
		7:00am MD Cleaners dba MD Restoration (LHPL)	5:00pm Centerplate: Tent Vendor Meeting (HR)	9:30am Army West Point Football Practice (Stadium)	1:00pm HHSAA Championships DII: 4:00pm HHSAA Championships DI: 7:00pm HHSAA	8:00am Swap Meet (Circle Lot) 7:30pm UH vs Army (Stadium)

December 2019

January 2020

Su	Mo	Tu	We	Th	Fr	Sa
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

December 2019

Su	Mo	Tu	We	Th	Fr	Sa
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
Dec 1	2	3	4 8:00am Swap Meet (Circle Lot)	5 8:00am Pay	6	7 8:00am Swap Meet (Circle Lot)
8 6:30am Swap Meet (Circle Lot) 5:30pm Catuquing Association party (HR)	9 9:00am HFD (Circle Lot)	10	11 8:00am Swap Meet (Circle Lot)	12 11:30am DAGS: Holiday Party (HR)	13	14 8:00am Play Sports (Stadium) 8:00am Swap Meet (Circle Lot) 6:00pm R.B.F. dba Sync
15 6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot) 8:00am Play Sports (Stadium)	16	17	18 8:00am Swap Meet (Circle Lot)	19 7:00am HCAP (HR) 8:30am Board Meeting (Admin Conf Rm)	20 8:00am Pay 5:00pm Bajet party (HR)	21 8:00am Swap Meet (Circle Lot) 6:00pm Torres party (HR)
22 6:30am Swap Meet (Circle Lot)	23	24 7:30pm HI Bowl (Stadium)	25 HOLIDAY - Christmas	26	27	28 8:00am Swap Meet (Circle Lot)
29 6:30am Swap Meet (Circle Lot)	30	31	Jan 1, 20	2	3	4

January 2020

February 2020

Su	Mo	Tu	We	Th	Fr	Sa
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29

January 2020

Su	Mo	Tu	We	Th	Fr	Sa
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
Dec 29	30	31	Jan 1, 20 Holiday - New Year's Day	2	3	4
5 6:30am Swap Meet (Circle Lot) 10:00am HI Tiki Bowl (Stadium) 5:00pm Niviera party	6 Holiday - Dr. Martin Luther King, Jr. Day 8:00am Color Vibe (Parking Lot)	7 Jr. Prep (Stadium)	8 Jr. Prep (Stadium) 8:00am Swap Meet (Circle Lot)	9 Jr. Prep (Stadium)	10 Jr. Prep (Stadium)	11 Jr. Prep (Stadium) 8:00am Swap Meet (Circle Lot)
12 6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot)	13	14	15 8:00am Swap Meet (Circle Lot)	16	17 8:00am Pay	18 8:00am Swap Meet (Circle Lot) 5:00pm Polynesian Bowl (Stadium)
19 6:30am Swap Meet (Circle Lot)	20 Holiday - Dr. Martin Luther King, Jr. Day 8:00am Color Vibe (Parking Lot)	21	22 8:00am Swap Meet (Circle Lot)	23 8:30am DOE: WASC Training (HR)	24	25 8:00am Swap Meet (Circle Lot)
26 6:30am Swap Meet (Circle Lot) 7:00pm Hula Bowl (Stadium)	27	28	29 8:00am Swap Meet (Circle Lot)	30 Pacific Rim Cup 2020 (Stadium)	31	Feb 1

February 2020

March 2020

Su	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
Mo																																
Tu																																
We																																
Th																																
Fr																																
Sa																																

February 2020

Su	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29		
Mo																															
Tu																															
We																															
Th																															
Fr																															
Sa																															

SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
Jan 26	27	28	29	30	31	Feb 1
6:30am Swap Meet (Circle Lot)	8:30am DLNR: Aviation Safety Training (HR)	8:30am DLNR: Aviation Safety Training (HR)	8:00am Pay 8:00am Swap Meet (Circle Lot) 8:30am DLNR: Aviation Safety Training (HR)	7:30am DHRD: Safety Office (HR)	7:30am DHRD - Safety Office (HR)	Pacific Rim Cup 2020 (Stadium) 8:00am Swap Meet (Circle Lot)
2	3	4	5	6	7	8
6:30am Swap Meet (Circle Lot)	8:30am DLNR: Aviation Safety Training (HR)	8:30am DLNR: Aviation Safety Training (HR)	8:00am Pay 8:00am Swap Meet (Circle Lot) 8:30am DLNR: Aviation Safety Training (HR)	7:30am DHRD: Safety Office (HR)	7:30am DHRD - Safety Office (HR)	8:00am Swap Meet (Circle Lot)
9	10	11	12	13	14	15
6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)
16	17	18	19	20	21	22
6:30am Swap Meet (Circle Lot)	Holiday - Presidents' Day 3:00am Great Aloha Run (Stadium)	8:00am DOE: Professional Development (HR) 8:00am Girl Scouts (cookie set-up)	8:00am DOE: Professional 8:00am Swap Meet (Circle Lot) 8:00am Girl Scouts	4:30am Girl Scouts (cookie distribution) (LHPL) 7:00am AMR (Bus Lot) 8:00am Pay	7:00am AMR (Bus Lot) 8:00am Girl Scouts (cookie break-down) (LHPL)	8:00am Swap Meet (Circle Lot)
23	24	25	26	27	28	29
6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)

March 2020

April 2020

Su	Mo	Tu	We	Th	Fr	Sa
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30		

March 2020

Su	Mo	Tu	We	Th	Fr	Sa
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
Mar 1 6:30am Swap Meet (Circle Lot)	2	3	4 8:00am Swap Meet (Circle Lot)	5 8:00am Pay	6	7 7:30am DOE: Driver & Traffic Safety Education (LHPL) 8:00am Swap Meet (Circle Lot)
8 6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot)	9	10	11 8:00am Swap Meet (Circle Lot)	12	13	14 8:00am Swap Meet (Circle Lot)
15 6:30am Swap Meet (Circle Lot)	16	17	18 8:00am Swap Meet (Circle Lot)	19	20 8:00am Pay	21 8:00am Swap Meet (Circle Lot)
22 6:30am Swap Meet (Circle Lot)	23	24	25 8:00am Swap Meet (Circle Lot)	26 7:00am DOE: Driver Excellence & Traffic Safety Fair (set-up) 7:45am Holiday - Prince Kuhio Day	27 7:00am DOE: Driver Excellence & Traffic Safety Fair (LHPL)	28 6:30am DOE: Driver Excellence & Traffic Safety Fair (LHPL) 8:00am Swap Meet (Circle Lot)
29 6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot)	30	31	Apr 1	2	3	4

April 2020

April 2020							May 2020						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
5	6	7	8	9	10	11	3	4	5	6	7	8	9
12	13	14	15	16	17	18	10	11	12	13	14	15	16
19	20	21	22	23	24	25	17	18	19	20	21	22	23
26	27	28	29	30			24	25	26	27	28	29	30
							31						

SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
Mar 29	30	31	Apr 1	2	3	4
6:30am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)	8:00am Swap Meet (Circle Lot)	8:00am Pay	8:00am Swap Meet (Circle Lot) 4:00pm Queveido party (HR)
5	6	7	8	9	10	11
6:30am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)	8:00am Swap Meet (Circle Lot)	Holiday - Good Friday	8:00am Swap Meet (Circle Lot)
12	13	14	15	16	17	18
6:00am SCCA (LHPL) 6:30am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)	8:00am Swap Meet (Circle Lot)		8:00am Swap Meet (Circle Lot)
19	20	21	22	23	24	25
6:30am Swap Meet (Circle Lot)	8:00am Pay		8:00am Swap Meet (Circle Lot)			Monster Truck (Stadium) 8:00am Swap Meet (Circle Lot)
26	27	28	29	30	May 1	2
6:30am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)	8:00am Swap Meet (Circle Lot)		

May 2020

June 2020

Su	1	2	3	4	5	6
Mo	7	8	9	10	11	12
Tu	14	15	16	17	18	19
We	21	22	23	24	25	26
Th	28	29	30			27

May 2020

Su	3	4	5	6	7	8	9
Mo	10	11	12	13	14	15	16
Tu	17	18	19	20	21	22	23
We	24	25	26	27	28	29	30
Th	31						

SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
Apr 26	27	28	29	30	May 1	2
6:30am Swap Meet (Circle Lot)	4	5	6	7	8	9
		7:00am DHRD - Safety Office (HR)	8:00am Swap Meet (Circle Lot)	7:00am AMR (Bus Lot)	7:00am AMR (Bus Lot)	Monster Truck (Stadium) 8:00am Swap Meet (Circle Lot)
10	11	12	13	14	15	16
6:30am Swap Meet (Circle Lot)			8:00am Swap Meet (Circle Lot)		5:00pm Campbell HS Grad (Stadium)	8:00am Swap Meet (Circle Lot) 5:00pm Pearl City HS Grad (Stadium)
17	18	19	20	21	22	23
6:30am Swap Meet (Circle Lot) 5:00pm Milliani HS Grad (Stadium)			8:00am Pay 8:00am Swap Meet (Circle Lot) 6:00pm Area HS Grad		6:00pm 50th State Fair (LHPL) 6:00pm Radford HS Grad (Stadium)	8:00am Swap Meet (Circle Lot) 4:00pm 50th State Fair (LHPL)
24	25	26	27	28	29	30
6:30am Swap Meet (Circle Lot) 12:00pm 50th State Fair (LHPL)	Holiday - Memorial Day 12:00pm 50th State Fair (LHPL)		8:00am Swap Meet (Circle Lot)		6:00pm 50th State Fair (LHPL)	8:00am Swap Meet (Circle Lot) 4:00pm 50th State Fair (LHPL)
31	Jun 1	2	3	4	5	6
6:30am Swap Meet (Circle Lot) 12:00pm 50th State Fair (LHPL)						

DAVID Y. IGE
GOVERNOR

CURT T. OTAGURO
COMPTROLLER



An Agency of the State of Hawaii

ROSS I. YAMASAKI
CHAIRMAN, STADIUM AUTHORITY

SCOTT L. CHAN
MANAGER

RYAN G. ANDREWS
DEPUTY MANAGER

November Stadium Board Meeting Marketing Update

Marketing will continue to promote and explore new opportunities for the Aloha Stadium. In addition, we continue to focus on the following items:

1. University of Hawaii Communications/Marketing/Advertising Coordination -

- Know before you go guide updated and distributed to media.
- Pregame entertainment coordination.
- VIP suite(s) coordination.
- Sponsorship Vendor Village onsite coordination.
- On air segments as needed with media to promote upcoming games/activities.
- On air iheart Radio giveaway coordination.
- Continuous social media monitoring and updating on Instagram, Twitter and Facebook.

2. High School Football Communications/Marketing/Advertising Coordination -

- Stadium Stars program coordination.
- Continuous social media monitoring and updating on Instagram, Twitter and Facebook.

3. Update and maintain website

- Continue to maintain and update the website with current events and information on a daily base.
- Continue to update ADA compliance and site improvement issues online.

4. Promote facility and events through social media and ongoing public relations efforts

- Continue to promote all other activities and events through social media outlets (Instagram, FB, Twitter, LinkedIn, YouTube-as needed).
- Continue to work with current clients to assist with their events and possible future events.

5. Miscellaneous

- Assist with PR campaigns and advertising for new stadium (NASED) as needed.
- Working with local promoters for potential events/concerts.
- Working with local companies for potential partnerships and cross-promotional events.
- Assist clients with marketing needs as needed upon request.
- Continue working with IMG and assist as needed with sponsorships, events and activities.
- Continue to meet weekly with Centerplate and Krysti Peacock/Moxie Agency to review and assist as needed for marketing swap meet updates.
- Continue facility upgrades in sports museum and plazas.
- Continue to coordinate stadium tours; public and private.

6. Upgrade facility/event collateral

- In-house: finalized photos and copy for fact sheets. Under review.

MONTHLY SECURITY REPORT TO THE BOARD

The following is a brief summary of security related incidents which occurred from October 1, 2019, through October 31, 2019.

Criminal Property Damage

On October 19, 2019, during the UH football game, a vehicle was damaged in the Upper Halawa Parking Lot. Honolulu Police Department (HPD) was called and an HPD Report was filed. The incident was captured by Aloha Stadium surveillance cameras and a copy of the video was provided to HPD, along with a possible name of the suspect.

Motor Vehicle Collision/Fled Scene

On October 20, 2019, during Swap Meet, a vehicle owner reported someone had damaged their vehicle, which was parked in the Upper Halawa Parking Lot. There was no note and no witnesses in the area. HPD was called and an HPD Report was filed.

UH Football versus Air Force Academy on October 19, 2019


Stadium Nurses reported 6 Medical Assistance Calls. Three calls were for Injured Cared For (ICF). In one case, the injured person suffered injuries to their hand in the Parking Lot. The injured person was evaluated and treated by Stadium Nurse, then released to the Sheriff Dept, related to a possible criminal case. In the second case, the injured person (Stadium Employee) was evaluated and treated by Stadium Nurse, then released to their Supervisor. The injured person was cleared by the Stadium Nurse to drive themselves to the Emergency Room. In the third case, the injured person was evaluated and treated by Stadium Nurse, then released to their friends to go watch the game.


Three calls were for Sick Cared For (SCF). In one case, the person feeling sick was evaluated and treated by the Stadium Nurse and Emergency Medical Technicians (EMTs), then transported to the Emergency Room via ambulance. In the second case, the person feeling sick was evaluated and treated by Stadium Nurse and EMTs, then released to their friend, who agreed to transport the person feeling sick to the Emergency Room. In the third case, the person feeling sick was evaluated and treated by the Stadium Nurse, then released to their family member, who agreed to drive the person feeling sick home.

OIA Football on October 26, 2019

Stadium Nurses reported 2 Medical Assistance Calls. Both calls were for Injured Cared For (ICF). In one case, the injured person and their life partner refused treatment from the Stadium Nurse and left the Stadium property. In the second case, the injured person was evaluated and treated by Stadium Nurse, then released to a family member, who agreed to transport the injured person to the Emergency Room.


Swap Meets in September 2019

Stadium Nurses reported 4 Medical Assistance Calls. All 4 calls were Injured Cared For (ICF). In one case, the injured person was evaluated and treated by Stadium Nurse, then released on their own. In the second case, the injured person was evaluated and treated by the Stadium Nurse, then released on their own to catch an Uber. In the third case, the injured person was evaluated and treated by the Stadium Nurse, then released on their own, with the advice from the Stadium Nurse to follow up at Urgent Care if the injury does not improve or gets worse. In the fourth case, the injured person was evaluated and treated by Stadium 

Nurse, then released to a family member, who agreed to transport the injured person to Urgent Care. 

Conclusion

Prepared and submitted by,



Neal O. Sakamoto, Stadium Security Officer
11-7-2019, 2155hrs

Engineering Dept. Report For
Stadium Authority Board Meeting
21 Nov 2019

1. **H&S 5 Work**
 - a. Work completed in all public areas. Work beneath stands continues, but does not affect operations.
2. **2019 Forensic Structural Study**
 - a. Will start when approved
 - b. Will be the basis for H&S Phase 6, which will not be funded with CIP money since it will not last for 10 years.
 - c. Design for Be completed by May 2020. Bids will be returned in time for NTP to be issued July 2020 when funding is approved by State Gov't.
3. **Cellular**
 - a. ATT looking to install more antennae and permanent cellular equipment to allow removal of COW in SW BSA.
 - b. ATT also looking to install small 5G cellular Antennae in parking lot. Preliminary drawings submitted.
4. **Maintenance Items:**
 - a. Various electrical repairs continue
 - b. Major Plumbing issues continue to be worked on.
 - c. Continuing parking lot spot repairs as needed
 - d. Spot repairs to seats as needed
5. **HART Work in Bus Lot**
 - a. Only work left is topsoil behind new concrete curbs.
6. **HART Station in Kam Lot**
 - a. Construction continues by NAN

**HAWAII SPORTS PROPERTIES
STADIUM AUTHORITY MEETING – NOVEMBER 21, 2019**

General Updates

- Our two priority renewals still awaiting signature are Bank of Hawaii and Heineken. Both are verbal agreements, but there have been some delays due to legal process. We hope to have both fully executed in the next week or two.
- We continue to have discussions with non-legacy partners and prospects to increase our sponsor base and partnership revenue. While looking to finalize outstanding agreements, we also have a keen eye on Spring discussions for the second half FY. Specifically, we are looking to cultivate new business via Q1/Q2 events (e.g. Monster Truck, Hula Bowl) to A) drive additional 19/20 revenue, and B) provide an entry platform for new sponsors leading into 20/21 partnership opportunities. Given the holiday season, we are aiming to advance these discussions as quickly as possible.

Signed Contracts (as of 11/12/19)

- Hawaiian Financial FCU, Gentry Homes, Hawaii Self Storage, Hamada Financial Group, Kelly Eisenberg, GEICO, First Hawaiian Bank, Wyndham, Honolulu Disposal Service, Toyota/Servco, Bite Squad, Midas, Saint Louis School, Kaiser, Hawaiian Electric, Par Hawaii, Jack in the Box, UHA Health Insurance, Raising Cane's, Anheuser-Busch, State Farm, Veterans United, UPW, Burger King, Army Recruiting, Altres Staffing

Verbal Agreements – Moving Towards Contract (as of 11/12/19)

- Heineken, Bank of Hawaii, VICIS, Humana

In Discussion

- Young's Market, Central Pacific Bank, T-Mobile, Saint Louis Alumni Association

Greg Salas, Associate General Manager
Hawaii Sports Properties
Gregory.Salas@HawaiiSportsProperties.com



Centerplate

Monthly Report Stadium Authority Meeting 11/21/2019

ALOHA STADIUM SWAP MEET AND MARKETPLACE Oct-19

Shopper Attendance:

October Monthly Attendance		Days Open	Daily Average	Coupons	Paid Attendance	Average Daily Paid Attendance
2018	73,076	13	5,621	25	73,051	5,619
2019	73,805	12	6,150	14	73,791	6,149
Difference	729	-1	529	-11	740	530
%	1%		9%	-44%	1%	9%

Vendor Attendance:

October Total Stall Count		Days Open	D,E, & F Total Stall Count	Daily Average Count	A,B,C Total Stall Count	Daily Average Count
2018	6,186	13	3,290	253	2,896	223
2019	7,818	12	3,928	327	3,890	324
Difference	1,632	-1	638	74	994	101
%	26%		19%	29%	34%	46%


Operations Information:

In 2018 there was 2 UH Football games with a modified set up. The modified Swap Meet has a decreased attendance thus reducing the daily averages.

In 2019 there was only 1 UH Football game and it was an early game, completely closing the Swap Meet. As a result, it is one less day open causing the average to be normal.

The Vendor stalls are affected in the same way as the attendance, in addition to, credits for the two storm closures hit in October 2018. This deflated October 2018 stall sales making it look like a large increase in 2019.

**Honolulu Rail Transit Project Update
November 21, 2019
Aloha Stadium Authority**

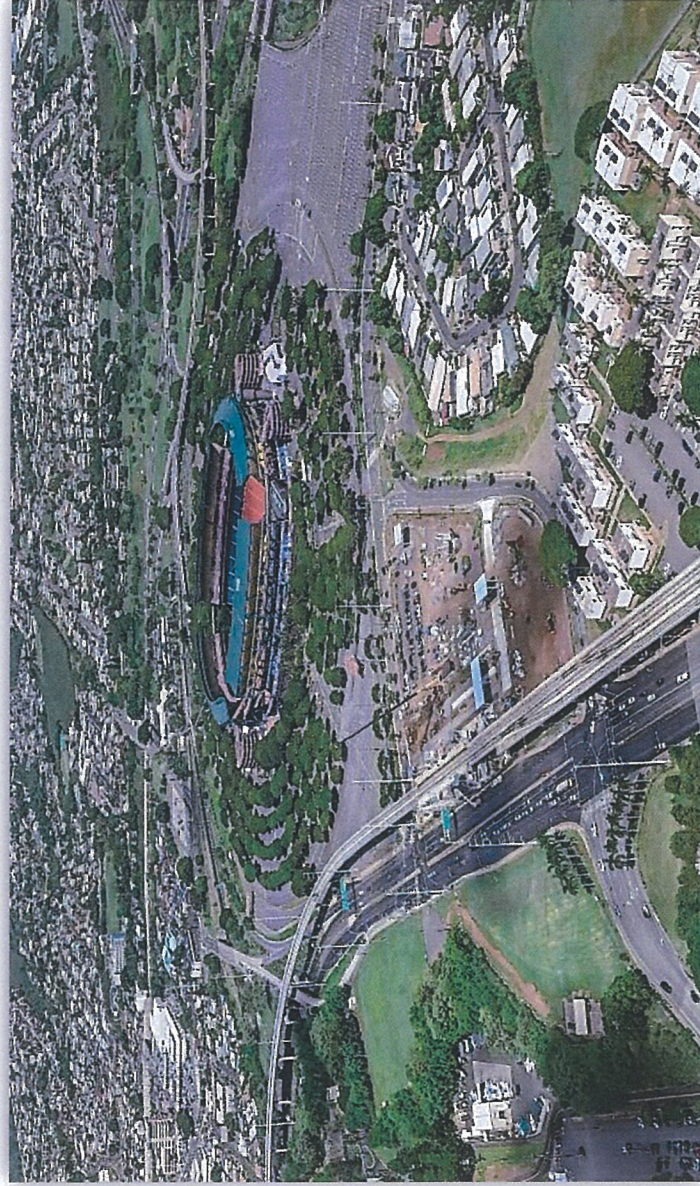




Status of Activities

Kamehameha Highway Stations Group

82% Complete

Substantial Completion projected for April '20
 Waiawa (Pearl Highlands) Station – 87% Complete

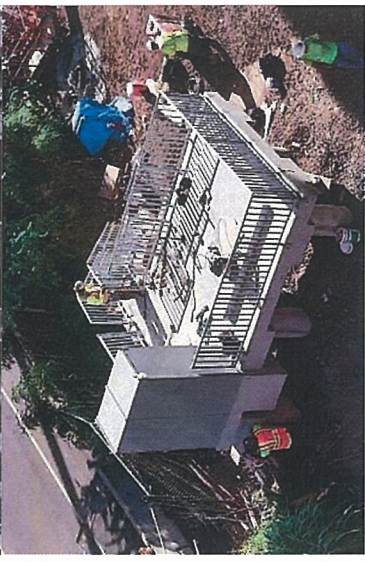

Major Work Remaining

- North entrance ramp & stairs
- Site slope & rock
- Elevators
- Canopies & fabric installation

Energization Status

- Station – December 2019

Core Systems Interface

- HRJV installing cable tray in TCCR
- BoS Date – Available for Comm work
- Conduit (GW to TCCR) – complete

- Platform Partial Access – November 2019
- Canopy Installation – December 2019

Kamehameha Highway Stations Group

82% Complete

Substantial Completion projected for April '20
 Kaluauo (Pearlridge) Station – 87% Complete



Major Work Remaining

- Faregate modules
- Elevators
- Canopies & fabric installation

Energization Status

- Station – November 2019

Core Systems Interface

- HRJV installing cable tray in TCCR
- BoS Date – November 2019
- Conduit (GW to TCCR) – complete
- Platform Partial Access – November 2019
- Canopy Installation – December 2019

Kamehameha Highway Stations Group

82% Complete

Substantial Completion projected for April '20
Halawa (Aloha Stadium) Station – 72% Complete



Core Systems Interface

- HRHJV working in TCCR
- BoS Date – November 2019
- Conduit (GW to TCCR) – complete

Major Work Remaining


- Edge pavers
- Entry plaza slab
- Parking lots
- Elevators
- Canopies & fabric installation

Energization Status


- Station – November 2019



Traffic

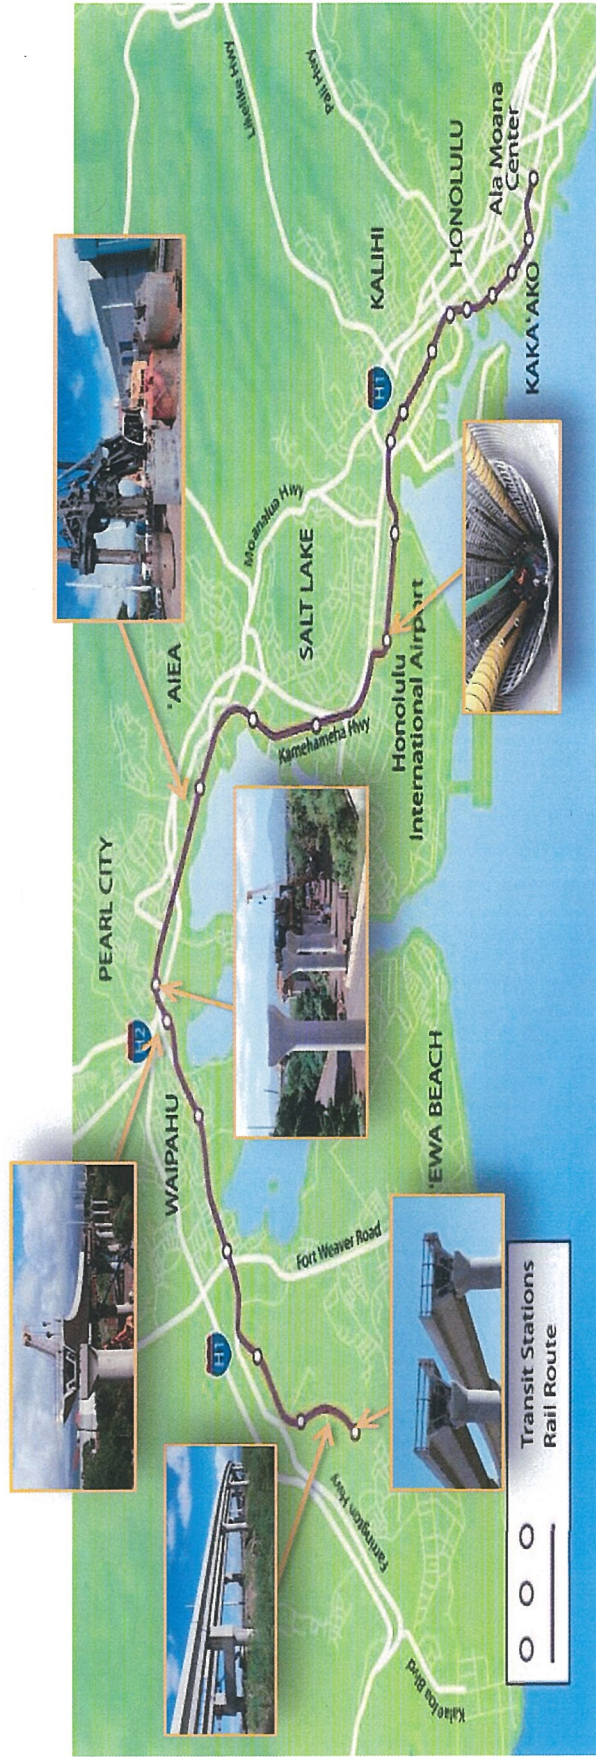

Airport Guideway and Stations Maintenance of Traffic Update

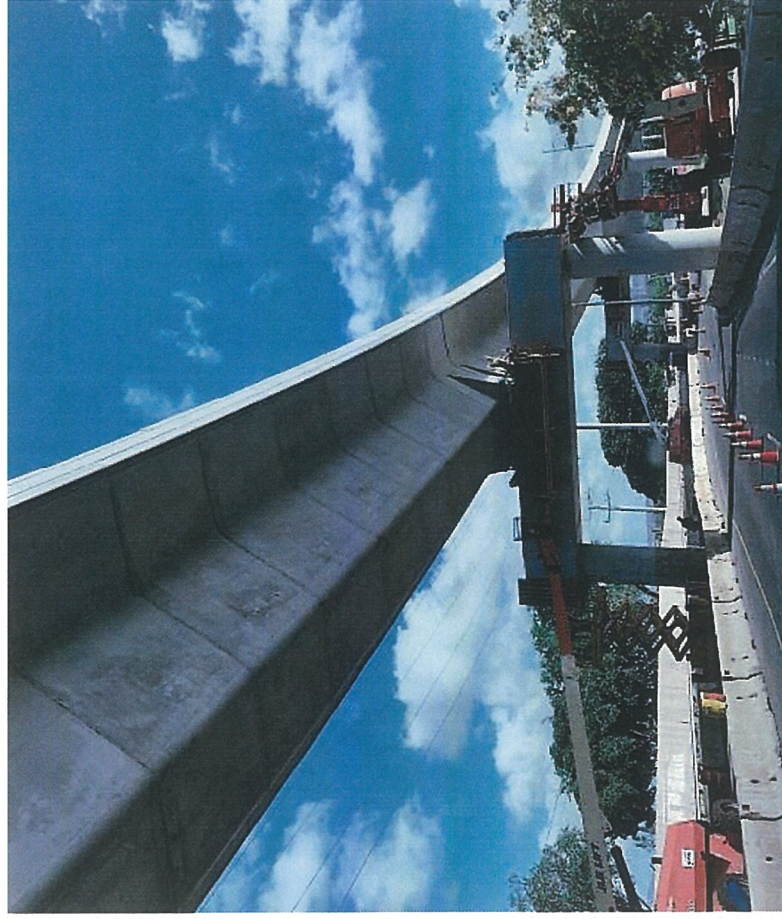

Kamehameha Highway

- **Day and night:** Daily single lane closures in both directions between Center Drive and Halawa to support gantry operations, station construction, guideway sound wall work and traffic signal trenching.

Nimitz Highway and Vicinity

- **Day/Night:** Intermittent closures along Nimitz Hwy Eastbound from Elliott Street to Aolele Street during second gantry operations and segment hanging.
- **Night:** Closures on Valkenburgh and Ualena Streets for utility relocations.

Airport Areas

- **Day/Night:** Alternating lane closures and 24-hour lane shifts from Aolele to Paiea Streets for airport utility work, shaft drilling, column erection, and ongoing station construction.
- **Night:** H-1 to Aolele Street off ramp closed. Lei stand detour configuration for column work. Flagging operations on Aolele Street east of Paiea for utility work.

Keehi Interchange


- **Night:** Lane closures along the H-1 and Nimitz ramp corridors in support of Reach E shaft drilling.



Project Wide Construction Update

West Oahu Stations Group 93% Complete

Substantial Completion projected for January '20
Kualaka'i (East Kapolei) Station – 89% Complete

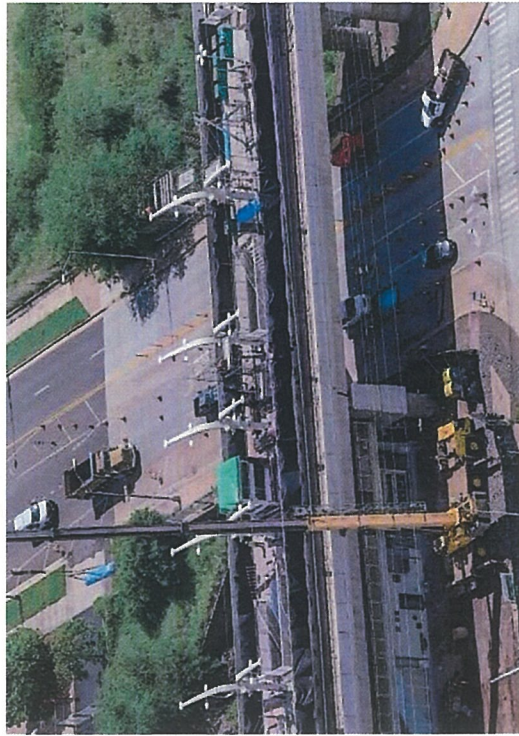

Core Systems Interface


- HRHJV working on the platform
- BoS Date – July 12, 2019
- TCCR Access – February 18, 2019

Major Work Remaining

- Faregate fabric
- Site utilities, grading, landscaping
- HVAC

Energization Status

- Station
 - Infrastructure – complete
- Energization – July 12, 2019

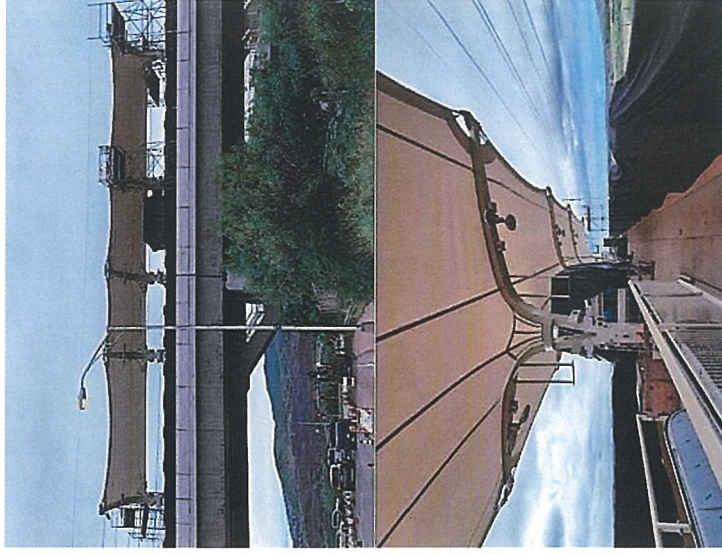

West Oahu Stations Group

93% Complete

Substantial Completion projected for January '20
Keone'ae (UH-West O'ahu) Station – 95% Complete



Core Systems Interface

- HRJV working in the TCCR and GW area
- BoS Date – March 18, 2019
- TCCR Access – February 2019



Major Work Remaining

- Canopy rework & fabric installation
- Site utilities, grading, landscaping
- HVAC

Energization Status

- Station
 - Infrastructure – complete
 - Pending HECO infrastructure work

- Platform Partial Access – June 4, 2019
- Canopy installation – December 2019
- Conduit (GW to TCCR) – May 2, 2019

West Oahu Stations Group


93% Complete

Substantial Completion projected for January '20
 Honouliuli (Ho'opili) Station – 94% Complete



Core Systems Interface

- HRJV pulling fiber & ATC cable in the TCCR area
- BoS Date – March 4, 2019
- TCCR Access – February 19, 2019

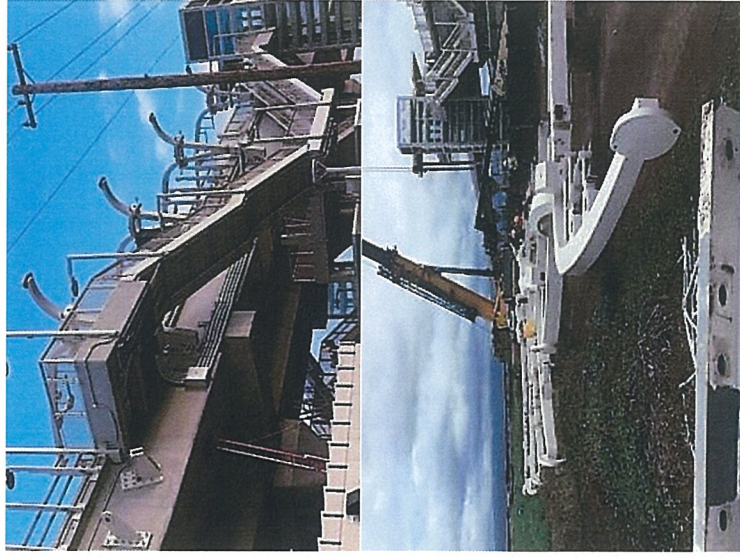

Major Work Remaining

- Fabric installation
- Faregate & civil site work
- Balustrades & fencing

Energization Status



- Station
 - Energized – March 7, 2019
- TPSS
 - Energized – February 20, 2019

- Platform Partial Access – April 9, 2019
- Conduit (GW to TCCR) – complete
- Canopy installation – November 2019

Farrington Highway Stations Group

93% Complete

Substantial Completion projected for December '19
 Hō'ae'ae (West Loch) Station – 93% Complete

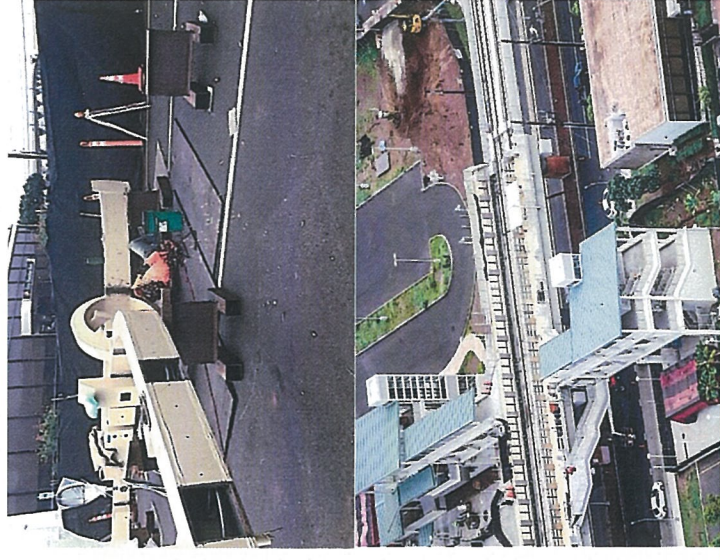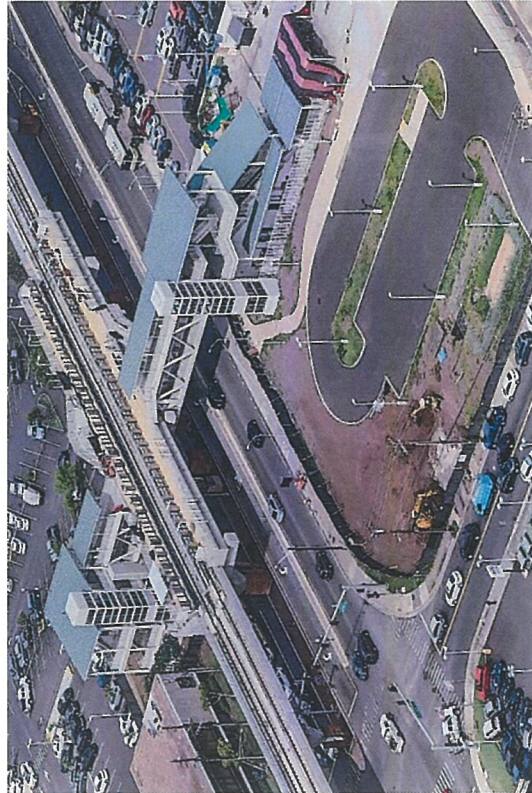

Major Work Remaining

- Entrance architectural slabs
- Faregate canopies & fabric installation

Energization Status

- Station and TPSS – complete


Core Systems Interface

- BoS Date – March 19, 2019
- TCCR Access provided
- Platform Partial Access – March 17, 2019
- Canopy installation – November 2019

Farrington Highway Stations Group

93% Complete

Substantial Completion projected for December '19
Pouhala (Waipahu Transit Center) Station – 92% Complete

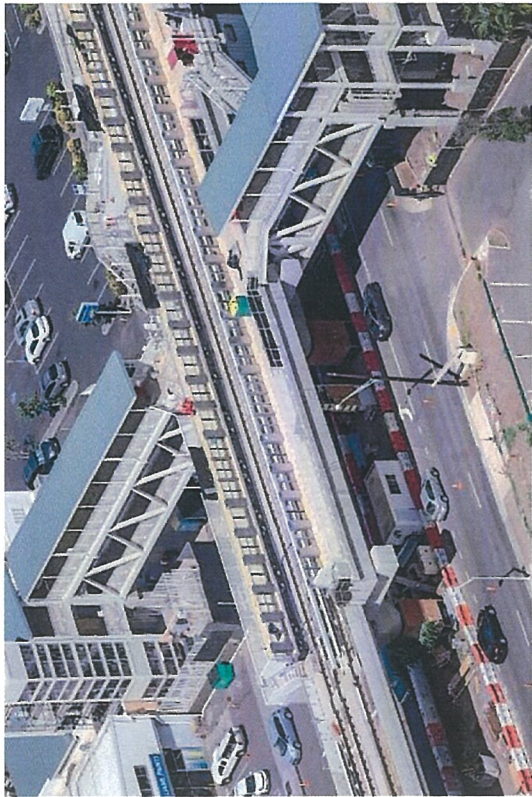

Major Work Remaining

- Moloalo Street entrance
- Faregate canopies & fabric installation

Energization Status

- Station and TPSS – complete

Core Systems Interface


- BoS Date – May 19, 2019 (FDAS)
- TCCR Access provided
- Platform Partial Access – March 2019
- Canopy Installation – December 2019



Farrington Highway Stations Group

93% Complete

Substantial Completion projected for December '19
 Hālaulani (Leeward Community College) Station – 94% Complete

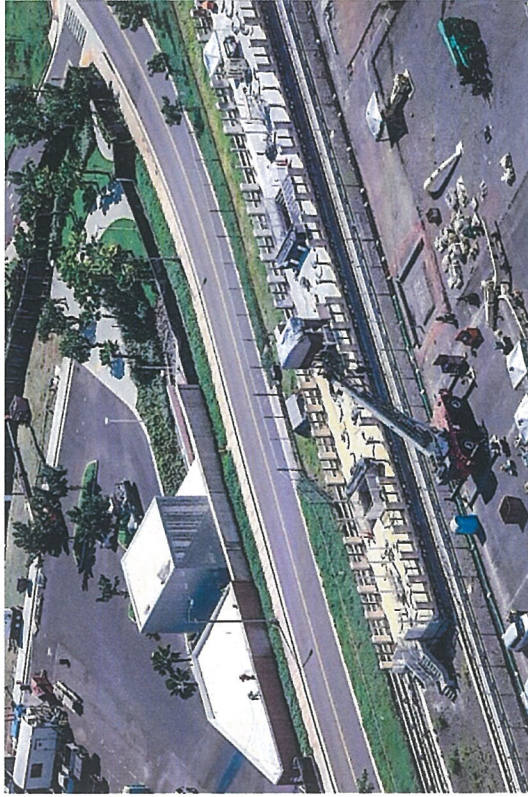

Core Systems Interface

- HRJV is currently working in the UPS room
- BoS Date – May 2019
- TCCR Access provided

Major Work Remaining

- Parking lot repairs
- Fabric installation
- Label electrical panels

Energization Status

- Station and GBS – complete



- Platform Partial Access – March 2019
- Canopy Installation – October 2019

University of Hawaii Park and Ride - Road "B"


82% Complete (85% Planned)

Substantial Completion projected for November '19



WOSG Group Interface

- Main power connection & tie into the UHWO Station
- Traffic signals

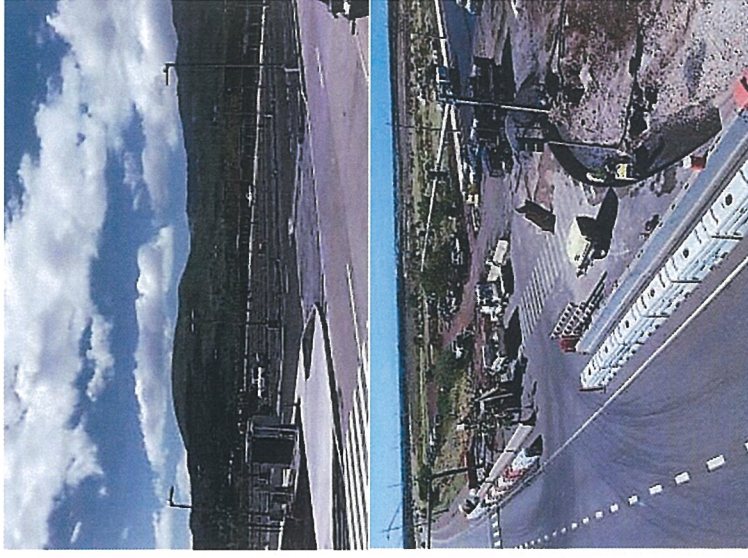

Major Work Remaining

- Electrical testing and acceptance of light poles and control cabinets
- Landscaping
- Punchlist



Core Systems 64% Complete

Projected Completion
4th Quarter 2025




MSF Yard

- ACS/IDS remedial work in the yard
- PIS cable remedial near completion
- CCTV formal SAT testing to begin at the end of November 2019
- CTS/SLAN site acceptance testing ongoing (58% complete)
- PA system preliminary tests

Passenger Vehicle

- Train #1: Start of lateral oscillation test at AW2
- Train #2: ATC testing in Functional Section
- Train #4: Start of RAT on test track
- Train #6: Leveling and weighing procedure
- Train #12: Delivered to site. First train for Interim Opening fleet

SEGMENT 1 - OVERALL INSTALLATION PROGRESS

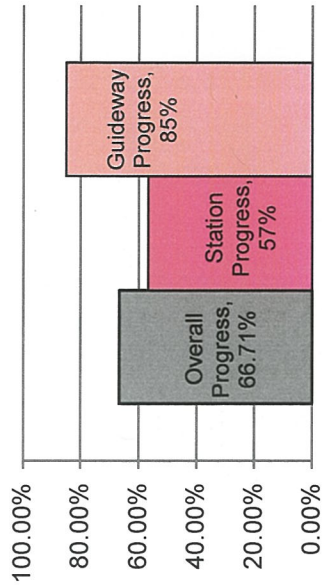


Core Systems

Interim Opening Progress

Installation 66%

Testing and Commissioning 20%

TESTING AND COMMISSIONING PROGRESS

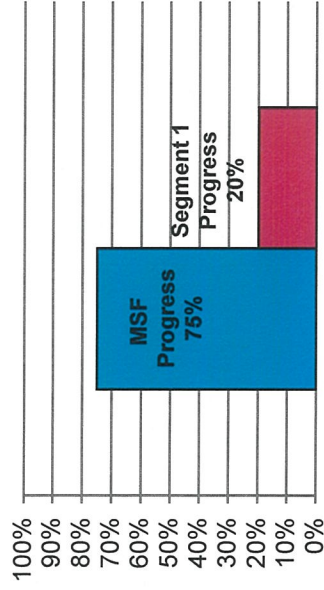

Installation

Ho'opili Station

- Communication installation
- FDAS installation

West Loch Station

- PSG electrical installation

Leeward Community College

- PSG mechanical installation - complete

Pearl Highlands

- UPS installation to start in November 2019

Pearlridge

- TES cable tray and cable pulling to begin mid-November 2019
- UPS installation

Aloha Stadium Station

- TEC cable tray installation - complete.
- Cable pulling

Testing and Commissioning

- Ho'opili PSG OSIT
- ATC wayside inter-station testing between TCCRs in the functional section
- SLAN and CTS testing in the yard
- CTP testing - complete
- WTP testing at EKP TCCR
- VTP testing in the Functional Section

Airport Guideway and Stations

57% Complete (59% Planned)

Production – Project-wide



Completed To Date

- Design progression at 99% (Earned value at 98% due to design resubmittals)
- 160 drilled shaft foundations
- 135 columns installed, and 64 spans have been erected
- 2,144 pre-cast segments have been cast

Major Work

- Reach A Guideway has progressed through the Pearl Harbor Station area
- HECO Zone 3: Existing OH lines on town side of intersection have been removed to allow P476 column work to proceed.
- Demolition and work zone preparation for Pier 551L to 557
- Reach C Guideway has progressed into the airport area
- Reach E: Shaft drilling continues at Pier 622. Demolition and removal of Moanalua Stream trestle continues. Mobilization and BMP installation at the Kalihi Stream trellis ongoing.
- HECO Zone 9: Electrical relocation work (HECO Duct 1652) on the Ewa side of Kalihi Stream was completed; drilling for Pier 627 in progress.

Airport Guideway and Stations

Makalapa (Pearl Harbor Naval Base Station) – 7% Complete

Work Planned for October

- Construct Makai column and Elevator 2 pit
- Construct the TCCR foundation

Work Completed in October

- Structural backfill at station entrance and TCCR.
- Underground mechanical and electrical work including City Fiber at the station entrance.
- Construct Makai column

Work Forecast for November

- Construct the TCCR foundation
- Install fire standpipe
- Construct Elevator 2 pit



Stay Connected

- Weekly Traffic Advisories
- Weekly e-Blast
- Website and Social Media



HART WEEKLY eNEWS

April 5, 2019

PROGRESS CONTINUES FOR STATIONS ALONG EWA-END OF THE PROJECT



Crews continue to make progress in completing the nine stations across the Ewa-end of the Honolulu Rail Transit Project.



HART Rapid Response

- 24-Hour Project Hotline number 808-566-2299
- Email inquiries info@HonoluluTransit.org
- Social Media inquiries

Mahalo!

HIC-TOD Report
For
Stadium Authority Board Meeting
21 Nov 2019

1. HIC-TOD Meeting held on 12 Nov 2019
 - a. Presentation on Creating, implementing a, and Maintaining Equitable TOD Community Development in HI, by LOCUS/Smart Growth America
 - b. Presentation on Honolulu Climate Change Guidelines
 - c. Permission was given to Chair to present Draft TOD Council Annual Report with Changes that are submitted buy 29 Nov 2019

2. December HIC-TOD Meeting Cancelled

New Aloha Stadium Entertainment District Committee (NASED)

November 15, 2019

Board Members: Brennon Morioka (Chair), John Fink, Keith Amemiya
Stadium Staff: Ryan Andrews, Charles Vitale, Stephen Lee

Purpose: Update Authority on various activities concerning NASED.

1. Governance

▫The first draft of the memorandum of agreement (MOA) formalizing the roles and responsibilities of HCDA, DAGS and Stadium Authority has been completed and reviewed. The document is now being revised and a second draft will be ready for review in early December.

2. Financial

▫Financial Advisor has been selected and the contract is in progress. Funding has been approved through the request for qualification (RFQ) phase.
 ▫Meetings between the consultant team, Stadium Authority, DAGS, HCDA and Office of Budget & Finance will be scheduled to discuss procurement/financial close requirements and processes.

3. ScheduleEnvironmental Impact Statement (EIS)

- End of extended EISPN comment period ended on 11/7/19.
- All data has been collected for various studies and draft reports are in progress.

Request for Qualifications (RFQ)

- Initial draft being review by stakeholders and consultants.
- Goal is to have committee appointed and RFQ released to market by end of year.

Master Planning

- First community master planning workshop scheduled for Wednesday, December 18, 2019, 7:00pm –9:00pm in the stadium Hospitality Room.
- Two additional community master planning workshops will take place in early 2020.

4. Communication and Public Engagement

Website – Continues to be updated. www.nased.hawaii.gov

Neighborhood Board and Community Association Meetings

- Aiea Neighborhood Board # 20 – November meeting cancelled due to Veterans Day holiday.
- Aliamanu/Salt Lake Board #18
 - Held on 11/14/19. Attended by stadium staff, DAGS staff and consultant team.
 - Provided updates related to EIS public comment period and invited the board to send representatives to the community master planning workshop on November 20, 2019.
- Aiea Community Association Meeting – Scheduled for November 21, 2019. Will be attended by representatives from stadium, DAGS and consultant team.
